

Our Redeemer's Lutheran Church

Vision Aligned Building (VAB) Update

June 1, 2021


The flooring in the Sanctuary and Chapel were completed last week. Most of the space is red oak, with slate inlays at the entry to the Sanctuary and north into the meeting room. The Chapel slate is also complete.



Chancel & Sanctuary



Chancel to Sacristy Steps

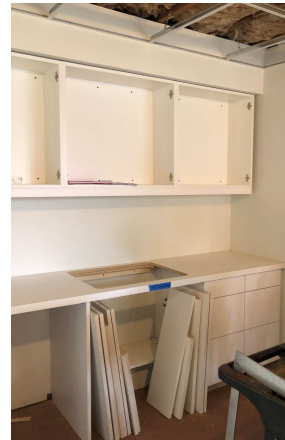

Kitchenette in Admin

Casework has been installed through the building and in Administration includes the new reception desk and bookcase, kitchenette, storage cabinets and worksurface. In the Sacristy, the cabinets and kitchenette are complete and waiting for the sink. Last week also saw the installation of the operable partition system in the Fellowship Hall that allows the space to be divided into two usable areas.



Administration Reception



Fellowship Hall Operable Partition

The reclaimed pews have been sanded and installation started today on the first wall of paneling and the bench under the long window wall. The week of 6/14, the contractor will begin the exterior site work including concrete and stair removal, grading, and the forming/pouring of the new entry and plaza and walkways. Paint in the Sanctuary will also begin the week of 6/14 with acoustical panels to follow.



PROJECT STATUS

Schedule: No Change - Church access late summer 2021

Date	Current Construction Contingency Balance	Current Project Contingency Balance
7/12/20	\$217,854	\$67,153
9/1/20	\$217,854	\$57,415
9/30/20	\$217,854	\$57,415
10/15/20	\$199,609	\$57,415
11/14/20	\$170,121	\$61,719
12/1/20	\$167,164	\$61,719
12/15/20	\$160,570	\$61,179
1/15/21	\$142,045	\$61,179
1/31/21	\$142,045	\$61,179
2/15/21	\$143,964	\$61,179
3/4/21	\$145,724	\$54,518
3/17/21	\$143,940	\$54,518
4/2/21	\$129,579	\$54,443
4/17/21	\$115,552	\$53,730
4/30/21	\$114,089	\$43,730
5/17/21	\$105,635	\$43,730
6/1/21	\$ 92,013	\$43,730

Changes affecting the Project Cost Contingency:

- Credit card charges for piano storage and moving expenses.
- Land sale attorney invoice (from September '20 – missed during move).
- Adjusted cost for groundbreaking event.
- Adjusted costs for moving.
- Created line item for Utilities. OR's pays utilities during construction (to avoid contractor markup). OR's operational budget has been paying costs and this line item will reimburse operational budget since bill have been higher than anticipated by that budget.

Charges against the Construction Contingency to date include:

- Lowering the Chapel floor to bring it to the same level as the Chancel and provide full ADA access.
- Providing a portable toilet with handwashing facilities for the Road to Housing clients for the duration of construction.
- Providing internet access to the site during construction due to removal required for service at new Ballard temporary finance office.
- Added framing and footing due to hidden conditions in framing at Narthex/Restroom area.
- Replace electrical conduit and wire that were in the Chancel floor framing.
- Chancel floor framing changes to due as-built condition
- Replace insulation in Administration area ceiling that was damaged by removal of asbestos popcorn ceilings.
- Add foundation and concrete costs due to lower-level concrete walls at south addition.

- Modification to Fellowship Hall Operable Wall to hang from beam vs. ceiling.
- Credit of \$400 for changing lower-level storefront and door to aluminum and adding electric strike.
- Revise Chapel north wall design
- Raise hydronic pipes in basement to eliminate damage potential.

- Wire replacement to meeting current codes and ensure warranties on new equipment.
- Electrical conduit and added outlets to support A/V systems and use in the building.
- Glaze two windows with opaque glass at lower level adjacent to new entry door.
- Reconcile bid allowance for improvements in Sacristy (credit)
- Delete acoustical panels in Fellowship Hall (credit)

- Reconcile bid allowance for drinking fountains (credit)
- Lighting fixtures – change due to ceiling configurations and availability of fixtures.



- Added cabinets and built ins for reception and office 119 (in lieu of furniture).
 - Credit for permitting fees not used in LZL's contract.
-

- Added steel at lower-level entry to support opening.
 - Add heater in room 08, exterior lighting a lower-level entry, change wiring for entry overhang lights.
 - Carpet at north stair from basement up to and including the 2nd floor room. Underlayment for organ room and balcony.
 - Added electrical for future light above baptismal font.
-

- Parge coat foundation walls at lower level, east entry.
 - Repair brick at NW corner (due to balcony beam), credit for grout (credit).
 - Replace NE Sanctuary exterior door.
 - Replace doors between Fellowship Hall and Narthex.
-

- East flat roofs repair to termination bars and waterproofing.
 - Replace handrail on north stair (3 levels).
 - Replace Narthex lighting.
 - Construct platform for organ.
 - Moved \$42K of \$50K site budget into construction contingency.
 - Added flatwork to Fellowship Hall and from 85th to entry plaza.
 - Site prep, grading, irrigation, landscape beds.
 - Added sidewalk widening and sweep entry along 85th.
-

- Paint Fellowship Hall exterior wood and repair/seal exterior beam ends.
- Structural reinforcement of Narthex window all.
- Paint lower-level corridor doors and frames.
- Recess structural bolts in Sanctuary floor.
- Add light cove at RC pew paneling.
- Allowance reconciliation at bench for radiant heat grills (credit) .

